

# GRP PROGRAM CONSTRUCTION PROGRESS



GRP Review  
Committee  
Meeting  
April 22, 2013




SJRA Board of  
Directors  
Meeting  
April 25, 2013

# ACCESS ROAD ASPHALT PROJECT CONSTRUCTION ADMINISTRATION

## Project Data Thru 03/31/2013 - Project Complete

Project Budget:	\$ 481,791.00
Contracted Amount:	\$ 413,829.00
Change Orders:	\$ [1,544.41]
Estimate to Complete:	\$ 412,284.59
Amount Invoiced:	\$ 412,284.59
Budget Remaining:	\$ 69,506.41
Percent In-Place Work:	100%
Completion Date:	March 28, 2013

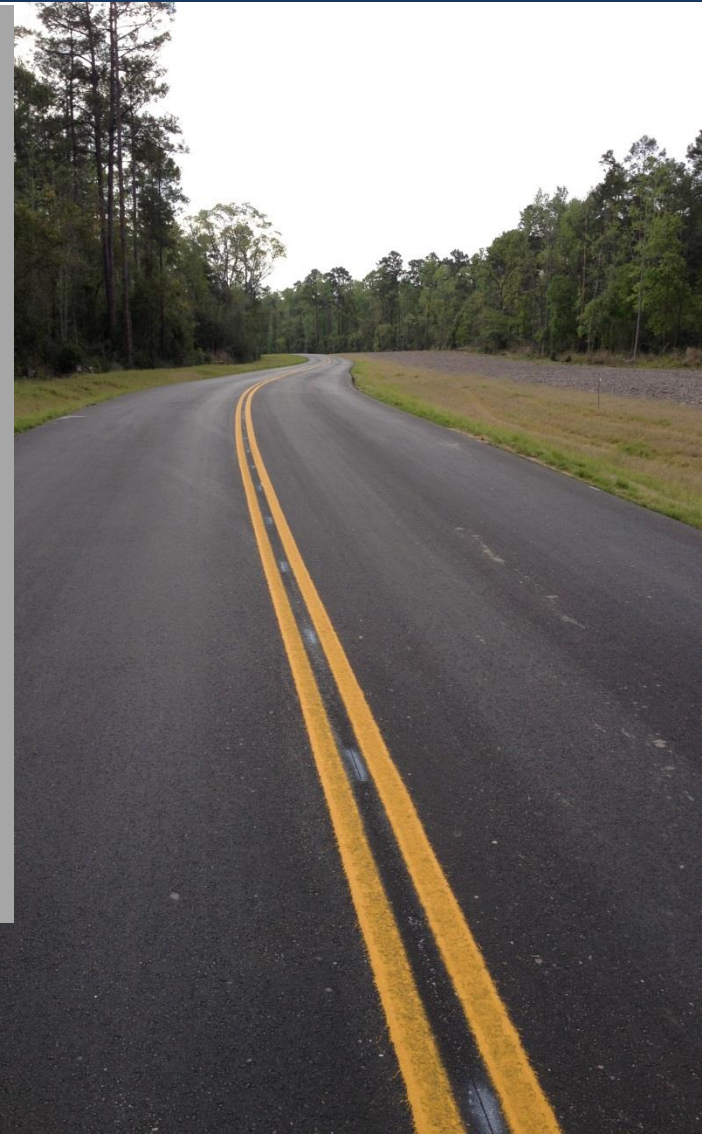



# SURFACE WATER FACILITY CONSTRUCTION ADMINISTRATION

## Project Data Thru 03/31/2013 - Early Work Package 4

Project Budget:	\$191,000,000.00
Contracted Amount:	\$190,704,740.00
Change Orders:	\$ 0.00
Estimate to Complete:	\$191,000,000.00
Amount Invoiced:	\$ 20,440,274.58
Budget Remaining:	\$170,559,725.42
Percent In-Place Work:	23.40%
Completion Date:	June 1, 2015



# RAW WATER INTAKE AND PUMP STATION



April 02, 2013

Raw Water Intake foundation forming system



# RAW WATER INTAKE AND PUMP STATION



April 09, 2013

Raw Water Intake foundation forming system



# RAW WATER INTAKE AND PUMP STATION



April 05, 2013

Concrete placement at Raw Water Intake bridge



# HIGH SERVICE PUMP STATION



March 04, 2013

March progress photograph of the Pump Room



# HIGH SERVICE PUMP STATION



April 04, 2013

Underground plumbing and electric installation



# HIGH SERVICE PUMP STATION



April 04, 2013

Stabilized soil backfill at the Discharge Bay



# GROUND STORAGE TANKS



March 06, 2013

March progress photograph at GST2



# GROUND STORAGE TANKS



March 28, 2013

Installation of interior concrete baffle walls at GST2



# WATER TREATMENT PLANT



March 15, 2013

March progress photograph at Granulated Activated Carbon Building



# WATER TREATMENT PLANT



April 01, 2013

Concrete encasement of piping at Granulated Activated Carbon Building



# WATER TREATMENT PLANT



March11, 2013

March progress photograph at Membrane Building



# WATER TREATMENT PLANT



Southeast pipe gallery at the Membrane Building



# WATER TREATMENT PLANT



April 02, 2013

42" Membrane feed piping from Pretreatment Facility



# WATER TREATMENT PLANT



March progress photograph at Pretreatment Facility



# WATER TREATMENT PLANT



April 01, 2013

Underground utility installation at Pretreatment Facility
