

WOODLANDS DIVISION

MONTHLY OPERATIONS REPORT

JUNE 2026



MONTHLY SUMMARY

We are pleased to report that the Woodlands Division experienced no unexpected expenditure for the month of June 2026.

On June 16, 2026, WWTP No. 1 experienced significant rainfall associated with Tropical Storm Arthur, receiving more than 7.8 inches of rain, including 6.5 inches within a two-hour period. The intense storm resulted in a peak influent flow of 29.09 million gallons (MGD). In line with regulatory requirements, we reported a 2-hour peak flow permit violation of 25.30 MGD to the Texas Commission on Environmental Quality (TCEQ). Staff continually monitors system performance and evaluates opportunities to reduce the impacts of extreme weather events on treatment operations.

Thank you to the Directors who attended the New MUD Director Woodlands Division Orientation on June 24, 2026. We look forward to hosting you at the GRP Tour in July.




A Look Ahead



- July 2026:** MUDS's Recommendation to Trustees for FY27 Woodlands Operating Budget
July 30, 2026 – New MUD Directors GRP Tour
- Aug 2026:** Woodlands Water Trustees Action for Approval of FY27 Woodlands Operating Budget




WATER PRODUCTION

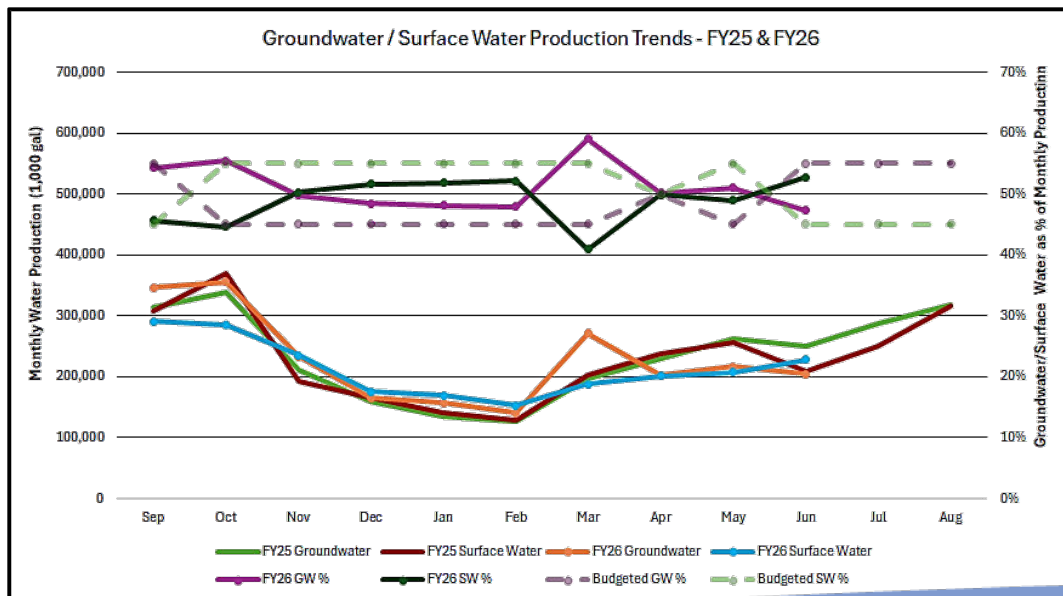

Production	Gallons (1,000)		Blend %		Budgeted %	
FY	Groundwater	Surface Water	Groundwater	Surface Water	Groundwater	Surface Water
2021	2,810,265	2,438,112	54%	46%	65%	35%
2022	3,601,249	2,303,308	61%	39%	65%	35%
2023	3,181,716	2,875,982	53%	47%	50%	50%
2024	2,820,645	2,775,491	50%	50%	50%	50%
2025	2,826,190	2,776,121	50%	50%	50%	50%
FYTD 2026	2,292,324	2,135,326	52%	48%	50%	50%

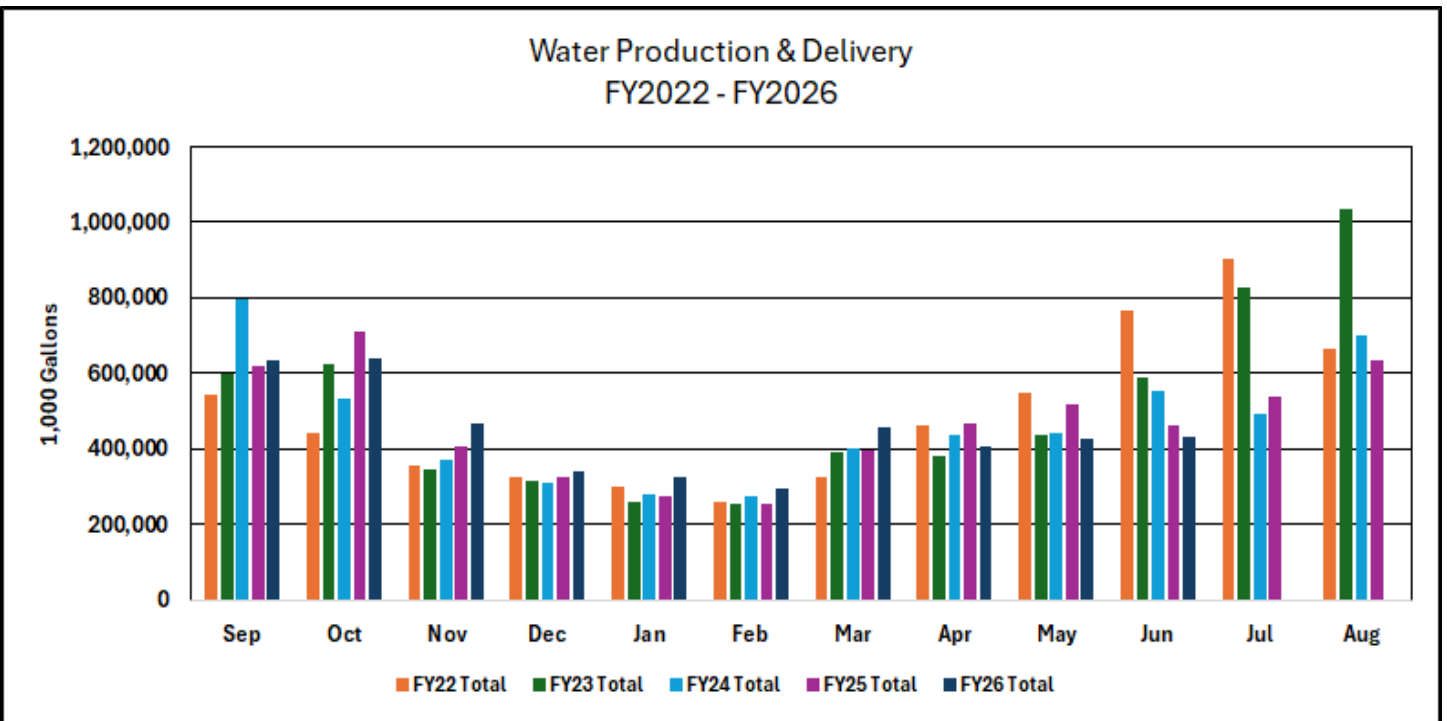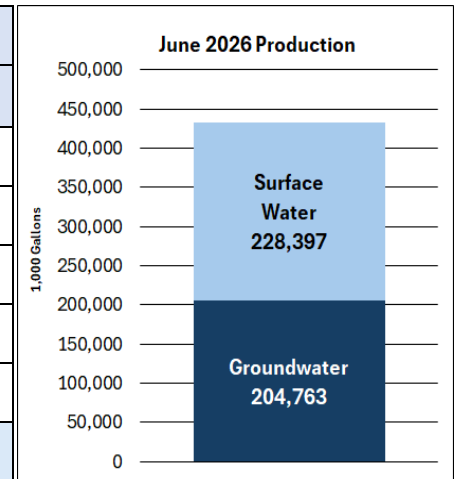

JUNE '26 SJRA Accounted for Water Loss (Gallons)			
Fire Flow	Flush	Break	Cause
	13,000		Dead-end main line flush
*Total Water Loss:		Rolling Year	Fiscal Year
		June 2025 – May 2026*	**FYTD 2026 (Aug'25-May'26)
SJRA Accounted Loss		0.141%	0.179%
Unaccounted Loss		5.965%	6.229%
Total Loss		6.106%	6.408%



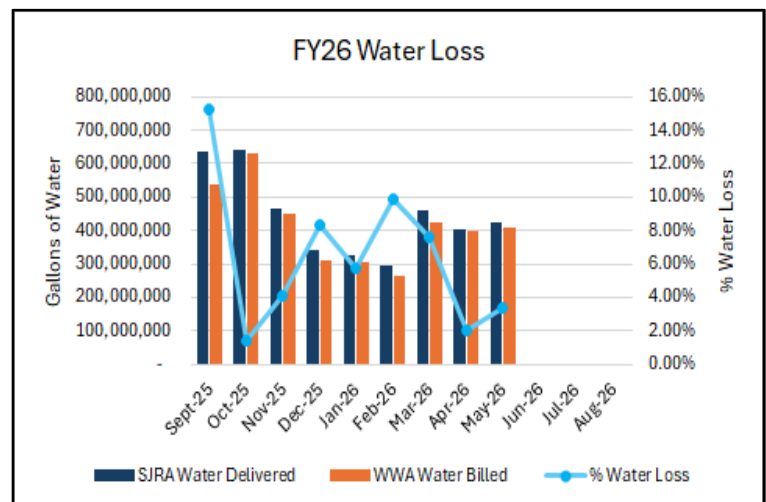


*Water Loss is one month behind due to timing of the monthly MUD billing data. **Water loss budgeted at **4.0%** for FY2026

WASTEWATER SYSTEM

The SJRA – Woodlands Division wholesale wastewater system contains three wastewater treatment facilities (WWTFs), 30 lift stations, 50 miles of gravity wastewater mains (15" and larger), and 20 miles of force mains from 4" to 24". These facilities are operated and maintained according to TCEQ and EPA rules and regulations as stated in facility specific permits, along with state and federal regulations.

SJRA Wastewater Treatment Facilities	Year Constructed	Permit Expires	Average Water Quality Tests Per Year	Discharges Into:
WWTF No. 1 2436 Sawdust Rd	1975	May 2027	3,012	Lower Panther Branch
WWTF No. 2 5402 Research Forest	1998, expanded 2005	May 2027	3,012	Upper Panther Branch
WWTF No. 3 555 Trade Center Pkw	1998, expanded 2003	May 2027	1,066	Unnamed tributary San Jacinto River

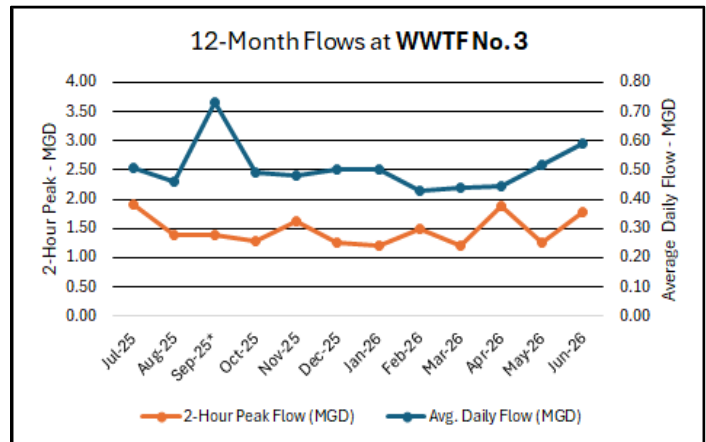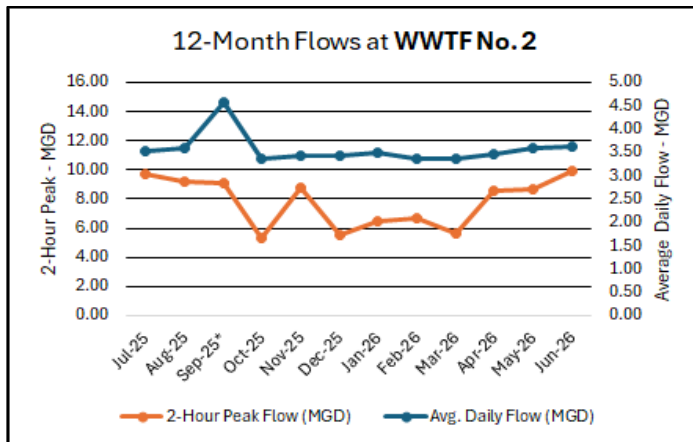
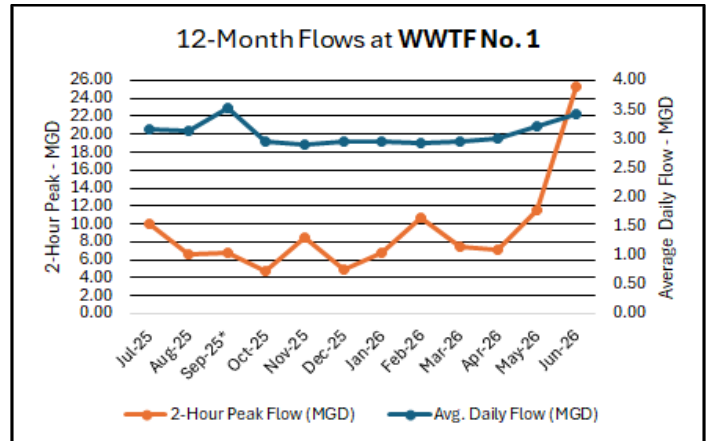


WWTF No. 1	Permit	Jul '25	Aug '25	*Sep '25	Oct '25	Nov '25	Dec '25	Jan-26	Feb '26	Mar '26	Apr-26	May-26	Jun '26
Avg. Daily Flow (MGD)	7.8	3.17	3.14	3.53*	2.96	2.91	2.95	2.95	2.93	2.94	3.01	3.21	3.43
2-Hour Peak Flow (MGD)	18	10.00	6.64	6.76	4.67	8.40	4.89	6.70	10.72	7.48	7.19	11.50	25.30
Chlorine (mg/l)	0.1	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.01
E. Coli (colonies per 100 ml)	200	8.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00
WWTF No. 2	Permit	Jul '25	Aug '25	*Sep '25	Oct '25	Oct '25	Dec '25	Jan-26	Feb-26	Mar '26	Apr-26	May-26	Jun '26
Avg. Daily Flow (MGD)	6	3.52	3.60	4.58*	3.35	3.44	3.43	3.51	3.37	3.35	3.46	3.59	3.61
2-Hour Peak Flow (MGD)	15.6	9.75	9.20	9.12	5.37	8.78	5.56	6.44	6.67	5.63	8.52	8.63	9.88
Chlorine (mg/l)	0.1	0.03	0.02	0.01	0.02	0.02	0.02	0.03	0.03	0.03	0.03	0.02	0.03
E. Coli (colonies per 100 ml)	200	1.00	14.00	6.30	6.30	10.90	3.10	2.00	1.20	2.00	1.00	3.10	3.10
WWTF No. 3	Permit	Jul '25	Aug '25	*Sep '25	Oct '25	Oct '25	Dec '25	Jan-26	Feb-26	Mar '26	Apr-26	May-26	Jun '26
Avg. Daily Flow (MGD)	0.9	0.51	0.46	0.73*	0.49	0.48	0.50	0.50	0.43	0.44	0.44	0.52	0.59
2-Hour Peak Flow (MGD)	3.6	1.91	1.40	1.40	1.28	1.61	1.26	1.21	1.49	1.21	1.88	1.27	1.77
Chlorine Minimum (mg/l)	1	1.53	1.21	1.20	1.04	1.14	1.17	1.11	1.04	1.04	1.09	1.04	1.23
Chlorine Maximum (mg/l)	4	2.73	3.89	3.84	3.74	3.19	3.10	3.80	3.75	3.79	3.89	3.89	3.68
E. Coli (colonies per 100 ml)	200	1.00	1.00	2.00	2.00	2.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00

*Note: Sept 2025 Flow Meter Calibration Error

INFRASTRUCTURE MAINTENANCE

JUNE 2026					
WORK ORDERS	# OF WORK ORDERS	HOURS SPENT	WORK ORDERS	# OF WORK ORDERS	HOURS SPENT
Preventive Maintenance (PM)	376	484.55	Corrective Maintenance (CM)	63	260.00
FYTD (SEPTEMBER 1, 2025 – JUNE 30, 2026)					
WORK ORDERS	# OF WORK ORDERS	HOURS SPENT	WORK ORDERS	# OF WORK ORDERS	HOURS SPENT
Preventive Maintenance (PM)	3480	6008.90	Corrective Maintenance (CM)	426	2465.35

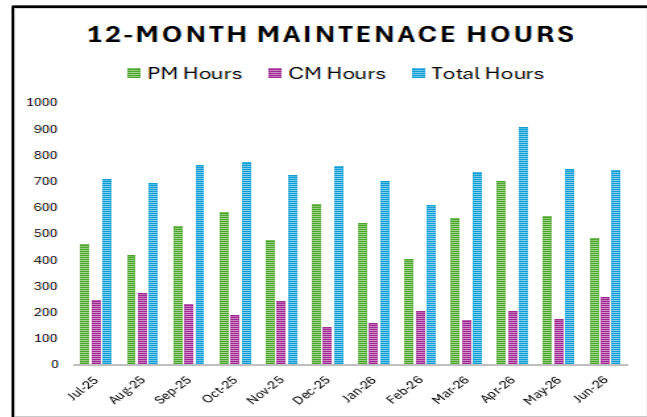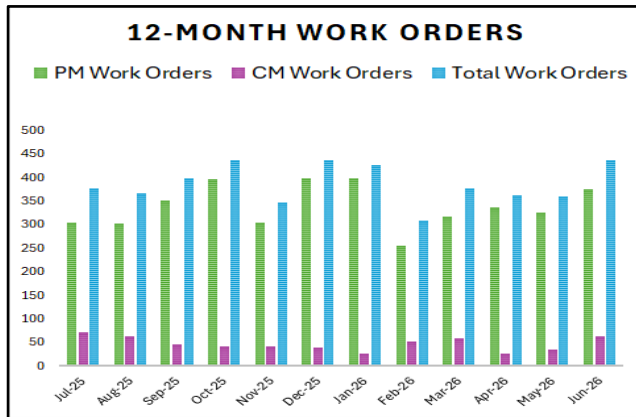

ASSET	LOCATION	PURPOSE	ISSUE	OUT OF SERVICE	IN SERVICE	SCHEDULE TO REPAIR
Aeration Basins 1 & 2	WWTF No. 1	Biological treatment of wastewater	Structural issues	03/01/2012	HOLD	To be demolished, awaiting Wastewater Master Plan
Wells 3 and 13	Varies	Raw water for treatment	All Pump failures	#3 03/25 #13 06/24		Wells 3 and 13 have been designed and construction contract has been awarded.
Wells 7, 15 and 30	Varies	Raw water for treatment	All Pump failures	#15 03/25 #7 03/24 #30 01/24		Wells 7, 15 and 30 are in design.
Low Head Filter No. 2	WWTF No. 2	Additional Solids Removal	Gear Drive Failure	11/21/2025		Filter offline for rehab. Repairs to gear drive will be done after rehab.
WAS Pump upgrades	WWTF No. 2	Waste activated sludge to digester.	Upsizing WAS pumps with old RAS pumps.	Remaining in service until new pump is installed in new pump slot	6/30/2026	The second WAS pump has been placed into service..
LS-16 Electrical and SCADA upgrade	Lift Station No. 16	Convey wastewater to the treatment facility.	Electrical & controls updates with implementing SCADA at this facility.	Site to remain in service while electrical rehab is underway.		Post for temporary panel has been installed. Waiting on other components to arrive.
Blower No. 3	WWTF No.3	Biological Treatment of Wastewater	Preplanned recondition due to age, before unit has a failure.	6/26/2026		Blower sent to repair shop for reconditioning.
Aeration Blower No. 2	WWTF No. 1	Biological Treatment of Wastewater	Soft start failure	6/19/2026	6/22/2026	Replaced soft start.
LS-1 ventilation shaft	WWTF No. 1	Evacuate gases and fumes from drywell of the lift station	Old galvanized duct had rusted out from corrosion	Site to remain in service while replacement is underway.		Continuing to fabricate new duct sections out of aluminum for corrosion resistance.
WW-21 Motor	WW-21 & 22	Power the well to pump water.	Motor Shorted	5/11/2026		Repaired motor to be delivered within the first week of July.

FINANCIALS

San Jacinto River Authority - Woodlands Operating
Actual to Budget Comparison
For the Nine Months Ending May 31, 2026

	May		YTD			Annual
	Actual	Budget	Actual	Budget	Variance	Budget
	(\$2,334,996)	(\$2,396,230)	\$27,235,031	\$25,700,529	\$1,534,502	\$40,779,048
OPERATING REVENUES						
OTHER REVENUES	\$53,491	\$8,330	\$513,971	\$75,000	\$438,971	\$100,000
OPERATING EXPENSES						
Salaries, Wages, & Employee Benefits	\$662,932	\$731,854	\$6,278,447	\$6,946,836	\$668,389	\$9,502,546
Professional Fees	27,656	53,949	300,268	486,562	186,294	648,475
Purchased & Contracted Services	1,248,259	1,346,808	12,333,911	11,660,315	(673,596)	17,781,275
Supplies, Materials & Utilities	493,892	536,280	4,164,056	4,728,354	564,298	6,570,895
Rentals	-	1,000	11,345	9,000	(2,345)	12,000
Maintenance, Repairs & Parts	150,753	218,817	1,211,476	1,970,137	758,662	2,626,850
General & Administrative Expenses	66,581	75,055	627,958	712,538	84,579	974,744
TOTAL OPERATING EXPENSES	\$2,650,072	\$2,963,763	\$24,927,462	\$26,513,743	\$1,586,281	\$38,116,784
NON-OPERATING EXPENSES	\$36,146	\$36,146	\$326,255	\$326,255	-	\$434,681
TOTAL EXPENSES	\$2,686,218	\$2,999,909	\$25,253,717	\$26,839,997	\$1,586,281	\$38,551,465
NET REVENUES OVER EXPENSES	(\$4,967,724)	(\$5,387,809)	\$2,495,285	(\$1,064,468)	\$3,559,753	\$2,327,583
CAPITAL IMPROVEMENTS	-	-	\$344,408	\$646,868	\$302,460	\$646,868
OTHER SOURCES (USES)						
Cash Sources (Uses)	\$ -	\$ -	\$ -	\$ -	\$ -	\$6,058,582
Bond Principal	(135,720)	(135,720)	(1,218,725)	(1,218,725)	-	(1,668,750)
Lease Principal	(795)	(795)	(7,088)	(7,088)	-	(9,487)
Repair and Replacement Transfers	(550,000)	(550,000)	(4,336,060)	(4,336,060)	-	(6,061,060)
TOTAL OTHER SOURCES (USES)	(\$686,515)	(\$686,515)	(\$5,561,874)	(\$5,561,874)	-	(\$1,680,715)
NET CASH BASIS SOURCES (USES)	(\$5,654,239)	(\$6,074,324)	(\$3,410,997)	(\$7,273,210)	\$3,862,213	-

Woodlands Division - SRF Bond:

	Original Issuance	Principal Balance	Principal due 10/1/26	Final Payment	Interest Rate
Series 2017	42,895,000	31,390,000	1,670,000.00	10/1/2042	0.00-1.710%

PROJECTS

Note: Design budget includes land acquisition, studies, preliminary engineering report (PER), final design, construction management, materials testing, and construction inspection. Projects in **yellow** are completed projects.

South Shore Gravity Main Rehabilitation	Location		Design		
	MUD 6		Budget	Contract	Invoiced
	The Trails north golf course, the Cove, across Woodlands Parkway to Lake Front Circle		\$1,999,321	\$988,929	\$552,621
			Completion Date:		Feb-2027
	Funding Source(s)		Construction		
	R&R	Bonds	Budget	Contract	Invoiced
	Phase		\$10,955,000	\$0	\$0
	Final Design		Estimated Start Date		May-2027

Design is 90% complete. Efforts are ongoing with the golf course and Montgomery County Precinct 3 to discuss construction logistics and secure temporary access and construction easements. Following this, SJRA will continue coordination with other external stakeholders to finalize the necessary temporary access and construction easements. Dates shown in table above are estimates and are subject to change based on ongoing efforts with the golf course.

WWTF No. 2 Tertiary Filters	Location		Design		
	MUD 67		Budget	Contract	Invoiced
	WWTF No. 2 (5402 Research Forest Dr.)		\$535,327	\$530,888	\$391,871
			Completion Date:		Nov-2025
	Funding Source(s)		Construction		
	R&R	Bonds	Budget	Contract	Invoiced
	Phase		\$5,366,000	\$5,366,000	\$3,707,063
	Construction		Estimated Completion Date		Oct-2026

Construction is in progress and on schedule. Contractor is continuing installation of filter equipment in basins 1 and 2, electrical and panelboard modifications, and drain piping. Start-up is expected in mid-July 2026.

Owners Advisor (Evaluation of WWTF No. 1 and Cost Comparison Study)	Location		Design		
	MUD 6		Budget	Contract	Invoiced
	WWTF No. 1 (2436 Sawdust Rd.)		\$834,096	\$833,776	\$547,490
			Completion Date:		On Hold
	Funding Source(s)		Construction		
	R&R		Budget	Contract	Invoiced
	Phase		NA	NA	NA
	Study		Estimated Start Date		NA

SJRA presented memorandum to the Woodlands Water Trustees/MUDs to move forward with a repair in place strategy for WWTF No. 1. This effort will include weighing the WWA SFDUE analysis and TCEQ rules and regulations to right-size future repair and replacement of structures and determine if a re-rating is needed to reduce the permitted capacity. The Woodlands Water Trustees approved moving forward with the initiative at their May 2026 meeting, followed by SJRA Board approval of the associated Professional Services Agreement (PSA) on May 28, 2026. A project kick-off meeting was held on June 9, 2026, and finalized meeting minutes were transmitted to WWA on June 25, 2026.

Lift Station No. 1 Gravity Main Bypass & Decommissioning	Location			Design		
	MUD 6 Northwest corner of Grogan's Mill and Woodlands Parkway			Budget	Contract	Invoiced
				\$387,711	\$193,987	\$182,275
				Estimated Completion Date:		Apr-2026
	Funding Source(s)			Construction		
	R&R	Bonds		Budget	Contract	Invoiced
	Phase			\$4,000,000	\$0	\$0
	Final Design			Estimated Start Date		Nov-2026
The final design has been approved by TCEQ and the County for demolition purposes. County engineering is currently reviewing the design. SJRA has met with Eastgate HOA and Woodlands Township to discuss disruptions to pavement and landscaping at the bypass tie-in location. SJRA is coordinating with the County and Howard Hughes on easement requirements.						

Town Center Water Line Replacement	Location			Design		
	MUD 6 & Metro Grogan's Mill between Woodlands Pkwy & Research Forest / Six Pines between N. Millbend & Timberloch / Lake Woodlands Dr. between Hughes Landing Blvd & Pinecroft Dr / Lake Front Circle between Lake Woodlands Dr. and Aviator's Way.			Budget	Contract	Invoiced
				\$2,118,629	\$1,879,731	\$1,348,132
				Estimated Completion Date:		Feb-2027
	Funding Source(s)			Construction		
	R&R	Excess Funds	Bonds	Budget	Contract	Invoiced
	Phase			TBD	\$0	\$0
	Final Design			Estimated Start Date		Mar-2027
The kick-off meeting for the re-design/added scope effort with the consultant occurred on September 22, 2025. The additional geotechnical and survey work has been completed and the design is underway. A draft construction method technical memo was submitted to SJRA on December 17, 2025, and SJRA provided comments on January 8, 2026. A revised construction method technical memo was submitted to SJRA on February 25, 2026, and comments were sent back on March 19, 2026. The first draft of the design for Lake Front Circle was received on May 15, 2026, and SJRA provided comments on May 27, 2026. Installation of casing crossings at intersections will utilize the CTPS method to bore larger casing pipe and slip in 12-inch water pipe.						

Water Plant Nos. 1, 2, & 3 Generator Replacement	Location		Design			
	MUD 36 & 47 Water Plant 1 - 11439 Slash Pine Water Plant 2 - 6140 Shadow Bend Water Plant 3 - 6698 Alden Bridge		Budget	Contract	Invoiced	
			\$138,519	\$224,311	\$116,301	
			Completion Date:		Mar-2025	
	Funding Source(s)		Construction			
	R&R			Budget	Contract	Invoiced
	Phase		\$3,314,082	\$3,222,568	\$2,471,614	
	Construction		Estimated Completion Date		Aug-26	

The generator has been placed into service and commissioned at Water Plant No. 2. The foundation and building work have been completed at Water Plant No. 1 and the 450kW generator moved from Water Plant No. 3 to Water Plant No. 1. The generator foundation for Water Plant No. 3 was completed on June 26, 2026.

Elevated Storage Tank No. 6	Location			Design		
	MUD 47			Budget	Contract	Invoiced
	Southeast corner of Egypt Ln. and Research Forest Dr.			\$1,938,687	\$1,143,621	\$616,692
				Estimated Completion Date:		Sep-2026
	Funding Source(s)			Construction		
	R&R			Budget	Contract	Invoiced
	Phase			\$9,469,000	\$13,750	\$13,750
Final Design			Estimated Start Date		Oct-2026	
Consultant is working on finalizing design and specifications for 100-percent submittal. SJRA and consultant working on addressing security and SCADA requirements. SJRA is coordinating with Entergy and Centerpoint for electricity and gas services to the site.						

WWTF No. 2 Grit Classifier	Location			Design		
	MUD 67 WWTF No. 2 (5401 Research Forest)			Budget	Contract	Invoiced
				\$106,540	\$146,392	\$108,859
				Estimated Completion Date:		Sep-2025
	Funding Source(s)			Construction		
	R&R	Excess Funds		Budget	Contract	Invoiced
	Phase			\$1,193,904	\$1,154,052	\$0
	Final design			Estimated Completion Date		Jan-2027
The construction contract and work orders for construction phase services and construction materials testing were approved at the December 2025 SJRA Board Meeting. Notice-to-proceed was given on February 16, 2026. Mobilization scheduled to commence on July 27, 2026. The grit classifier equipment is on order.						

Water Well Nos. 3 and 13 Rehabilitation	Location		Design (In-House)		
	MUD 6 & 47 Well No. 3 – 36 Secluded Trail Well No. 13 - 6698 Alden Bridge Dr.		Budget	Contract	Invoiced
			\$54,000	\$7,356	\$0
			Estimated Completion Date:		Apr-2026
	Funding Source(s)		Construction		
	R&R		Budget	Contract	Invoiced
	Phase		\$1,071,000	\$0	\$0
	Procurement		Estimated Start Date		Jul-2026
The temporary construction easement from the golf course for work at Water Well No. 3 was received on February 25, 2026. The notice of alteration from LSGCD for work on the two wells was approved on April 15, 2026. One construction proposal was received on May 27, 2026, for Weisinger Inc. and was recommended for SJRA Board approval.					

Woodlands Digital Water System	Location			Design		
	All Montgomery County MUDs in The Woodlands			Budget	Contract	Invoiced
				\$350,000	\$266,353	\$149,546
				Estimated Completion Date:		Apr-2026
	Funding Source(s)			Construction		
	R&R			Budget	Contract	Invoiced
	Phase			N/A	N/A	N/A
	Design			Estimated Start Date		N/A
Phase 3 includes access to an SJRA WaterSight module which will allow for interaction with the Woodlands Division water model and allow for running of scenarios and predictive analysis. A training of the WaterSight software was held on February 24-25, 2026. The Consultant is continuing to add scenarios and functionality to the WaterSight software. The Consultant is coordinating with SJRA IT to transfer program to SJRA's network.						

Woodlands Division Disinfection Byproducts (DBPs) Study	Location			Design		
	All Montgomery County MUDs in The Woodlands			Budget	Contract	Invoiced
				\$75,000	\$73,365	\$73,365
				Estimated Completion Date:		Apr-2026
	Funding Source(s)			Construction		
	Cash			Budget	Contract	Invoiced
	Phase			N/A	N/A	N/A
	Design			Estimated Start Date		N/A

This project will provide an evaluation of DBP levels for several scenarios for the five water service areas with and without mitigation measures at the GSTs and ESTs. For each mitigation strategy, cost estimates will be produced to show a cost/benefit relationship between DBP reduction and capital investment. The Consultant submitted the draft DBP study report on March 16, 2026, and SJRA provided comments back on April 1, 2026. The Consultant requested additional data from SJRA to answer several questions. The final report was received on April 27, 2026. This project has been closed and the final invoice received on June 10, 2026.

Lift Station No. 24 Improvements	Location			Design		
	MUD 60 Flintridge Drive, west of Kuykendahl Road			Budget	Contract	Invoiced
				\$526,000	\$174,821	\$120,521
				Estimated Completion Date:		FY 2027
	Funding Source(s)			Construction		
	R&R	Grant		Budget	Contract	Invoiced
	Phase			\$1,907,000	\$0	\$0
	Preliminary Design			Estimated Start Date		FY 2028

This project will consist of improvements to Lift Station No. 24 to reconfigure the site to mitigate the effects of future flooding. Preliminary design kicked off January 2026 with the design Consultant. SJRA received a draft Preliminary Engineering Report (PER) from the Consultant and provided comments; Consultant is addressing the comments and developing the Final PER. Draft PER was provided to the U.S. Army Corps of Engineers (providing grant funding) and awaiting feedback.

Elevated Storage Tank Inspection	Location			Study		
	MUDs METRO, 6, 39, 46, 47, 60 Various Sites throughout The Woodlands			Budget	Contract	Invoiced
				\$25,000	\$20,735	\$20,735
				Estimated Completion Date:		Jun-2026
	Funding Source(s)			Construction		
	Cash			Budget	Contract	Invoiced
	Phase			N/A	N/A	N/A
	Study			Estimated Start Date		N/A

This project involves a comprehensive inspection by the elevated storage tank consultant to assess the condition of the structural, mechanical, electrical and coatings of each of the six elevated storage tanks (EST) in the Woodlands Division system. The inspection data is being developed into a report to give results of the findings, recommendations for any repairs, and a schedule and budget for needed rehabilitation for each EST. Inspection of all six ESTs were completed by March 4, 2026. The draft inspection was received on April 13, 2026, and comments were sent back for revision on April 23, 2026. A second draft was received on May 8, 2026. Also, a follow-up inspection was done at EST No. 7 following a leak on the riser pipe. This inspection was incorporated into the second draft. The final report was submitted to SJRA on June 1, 2026. The final invoice has been submitted, and the project is ready for close-out.

Lift Station No. 21 Force Main Renewal	Location			Design		
	MUD 6 Along Grogans Mill Road South of Sawmill			Budget	Contract	Invoiced
				\$94,000	\$151,900	\$0
				Estimated Completion Date:		May-2027
	Funding Source(s)			Construction		
	R&R			Budget	Contract	Invoiced
	Phase			\$531,000	\$0	\$0
	Preliminary Design			Estimated Start Date		Jul-2027
This project will consist of rehabilitating or replacing the deteriorated force main of Lift Station No. 21. A Professional Services Agreement and Work Order No. 1 for preliminary design was approved at the March 2026 SJRA Board of Directors meeting. A kickoff meeting with the Consultant was held on April 8, 2026. The Consultant has been working on the alternatives analysis for 3 rehab methods and will present them at a workshop for the SJRA on July 8 and provide a recommendation for the best rehab.						

Lift Station No. 5 Force Main Replacement	Location		Design			
	MUD 6 & 7 Between Lift Station No.5 and WWTF No. 1		Budget	Contract	Invoiced	
			\$399,938	TBD	\$0	
			Estimated Completion Date:		Jul-2027	
	Funding Source(s)		Construction			
	R&R			Budget	Contract	Invoiced
	Phase		\$9,100,062	TBD	\$0	
	Final Design		Estimated Start Date		Nov-2027	
In March 2026 the Woodlands MUDs and Trustees voted in favor of replacing the Lift Station No. 5 force main and reallocating \$9.5 million from WWTF No.1 Land Acquisition project to the Lift Station No.5 Force Main Replacement project. Project is being re-initiated. ARKK Engineers is the Firm the SJRA plans to utilize to review data, update surveys for current improvements along the route, and update the final design for construction. Temporary access/construction easements will need to be obtained, and the consultant will be responsible for defining those easements. Project planned to restart in August 2027.						

WOODLANDS ACRONYMS AND DEFINITIONS

FY Fiscal Year
FYTD Fiscal Year To Date
MGD Million Gallons Per Day
SJRA San Jacinto River Authority
TCEQ Texas Commission on Environmental Quality

SJRA WO Division

Located in southern Montgomery County, the Woodlands Division provides wholesale water supply and wastewater treatment services to the 100,000-plus population of The Woodlands through the financing, construction, operation, and maintenance of three regional wastewater treatment plants, a wastewater conveyance system with 30 lift stations, 5 water plants, 37 water wells, 6 elevated and 9 ground storage tanks, and miles of wastewater collection and potable water distribution lines.

SJRA GRP Division

Division of the SJRA responsible for GRP compliance, and the management, administration, operation and maintenance of the surface water facilities and surface water transmission system. The GRP Division operates and maintains a 30 MGD surface water treatment facility and 55 miles of transmission water lines.

Surface Water

Surface water comes from rivers and lakes and receives a high degree of treatment and disinfection prior to being distributed to customers. The Woodlands Division receives water from the SJRA GRP Division that treats raw water from Lake Conroe.

Groundwater

The water that fills cracks, voids, and other openings in beds of rocks, sand, and soil is called groundwater. It is found in soils and sands that can retain the water - much like a sponge holds water - and is constantly replenished by rainfall or snow. The Woodlands Division has active groundwater wells in the Evangeline and Jasper aquifers.
